



Conservation Cover - General

Conservation Cover Job Sheet

PA327

Landowner _____ Tract No. _____ Field No.(s) _____ Acres _____


Purpose (check all that apply)	
<input type="checkbox"/> Reduce soil erosion and sedimentation	<input type="checkbox"/> Enhance wildlife habitat
<input type="checkbox"/> Improve soil quality	<input type="checkbox"/> Manage plant pests
<input type="checkbox"/> Improve water quality	<input type="checkbox"/> Improve air quality

Refer to Technical Guide Reference No. 122 for recommended seeding mixtures				
Layout	Field border 1	Field border 2	Field border 3	Field border 4
Area (acres)				
Species #1				
Species #2				
Species #3				
Species #4				
Seeding rate (pure live seed* – lbs/acre) *only for native warm-season grasses				
Lime (tons/acre)				
N (bs/acre)				
P ₂ O ₅ (lbs/acre)				
K ₂ O (bs/acre)				

Site Preparation
<i>Prepare a weed-free seedbed. Apply lime and fertilizer as indicated by soil testing. Additional requirements:</i>
Planting Method
<i>Drill grass and legume seed _____ inches deep uniformly over area. Establish vegetation according to the specified seeding rate. If necessary, mulch newly seeded area with _____ tons per acre of mulch material. When needed, plant a small grain nurse/companion crop at the rate of _____ pounds per acre (clip or harvest before it heads out). Additional requirements:</i>
Operation and Maintenance
<i>Inspect and repair field borders after storms to fill in gullies, remove sediment, and/or reseed disturbed areas as needed. Do not mow during the nesting season (May through July).</i>

If needed, an aerial view or a side view of the practice can be shown below. Other relevant information, complementary practices and measures, and additional specifications may be included.

Scale 1"=_____ ft. (NA indicates sketch not to scale: grid size=1/2" by 1/2")

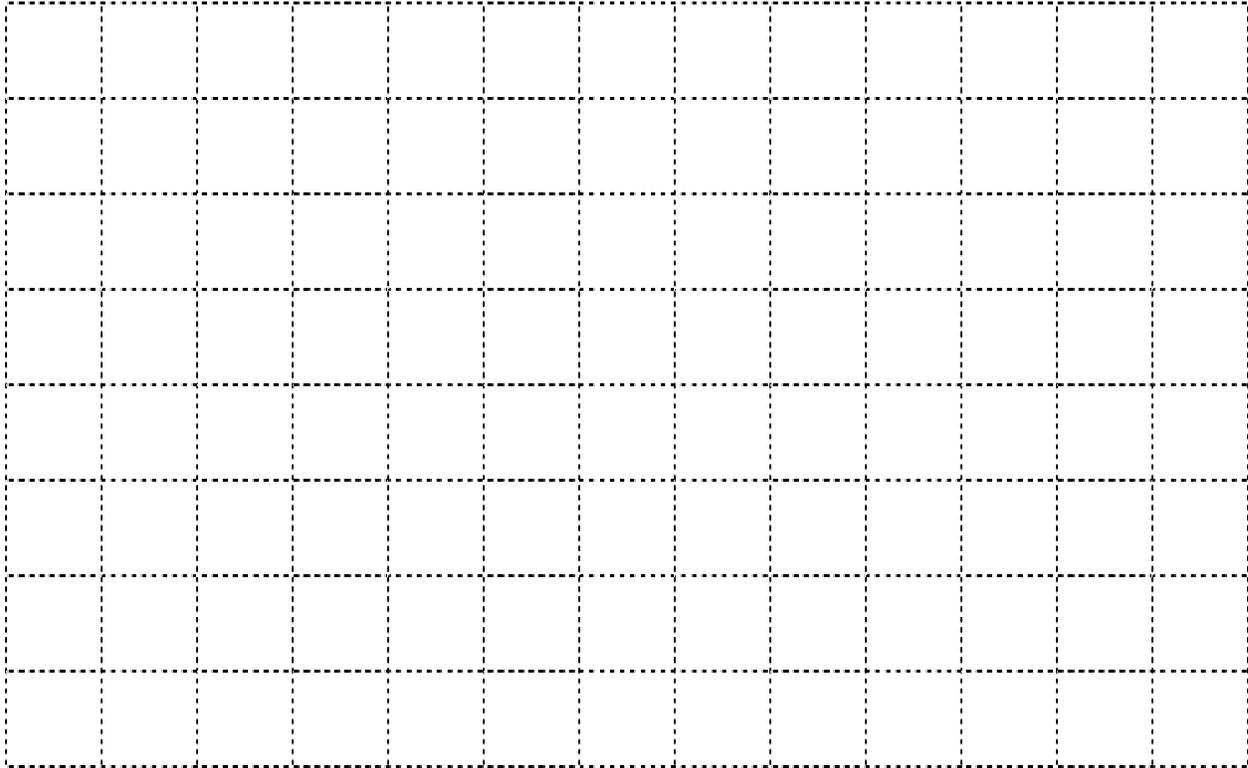

Additional Specifications and Notes:

Check Out and Certification Requirements:

I certify that the above Planting Specifications and Installation requirements _____ have _____ have not been met in accordance with the criteria of the NRCS PA Conservation Practice Standard PA 340. The total of _____ acres of this practice were installed on the locations covered by this job sheet on the date(s) of _____.

Signature Designated Conservationist or Technical Service Provider Date
